


Item	Activity
1	Re-phase traffic signals at Knowledge Gateway
2	New carriageway
3	Drainage
4	Earthworks
5	New pedestrian crossing
6	Vehicle restraint system

Item	Activity
7	Landscaping
8	Retaining walls
9	Footways & cycleways
10	Traffic signals
11	Signage & streetlighting
12	Surfacing & road markings

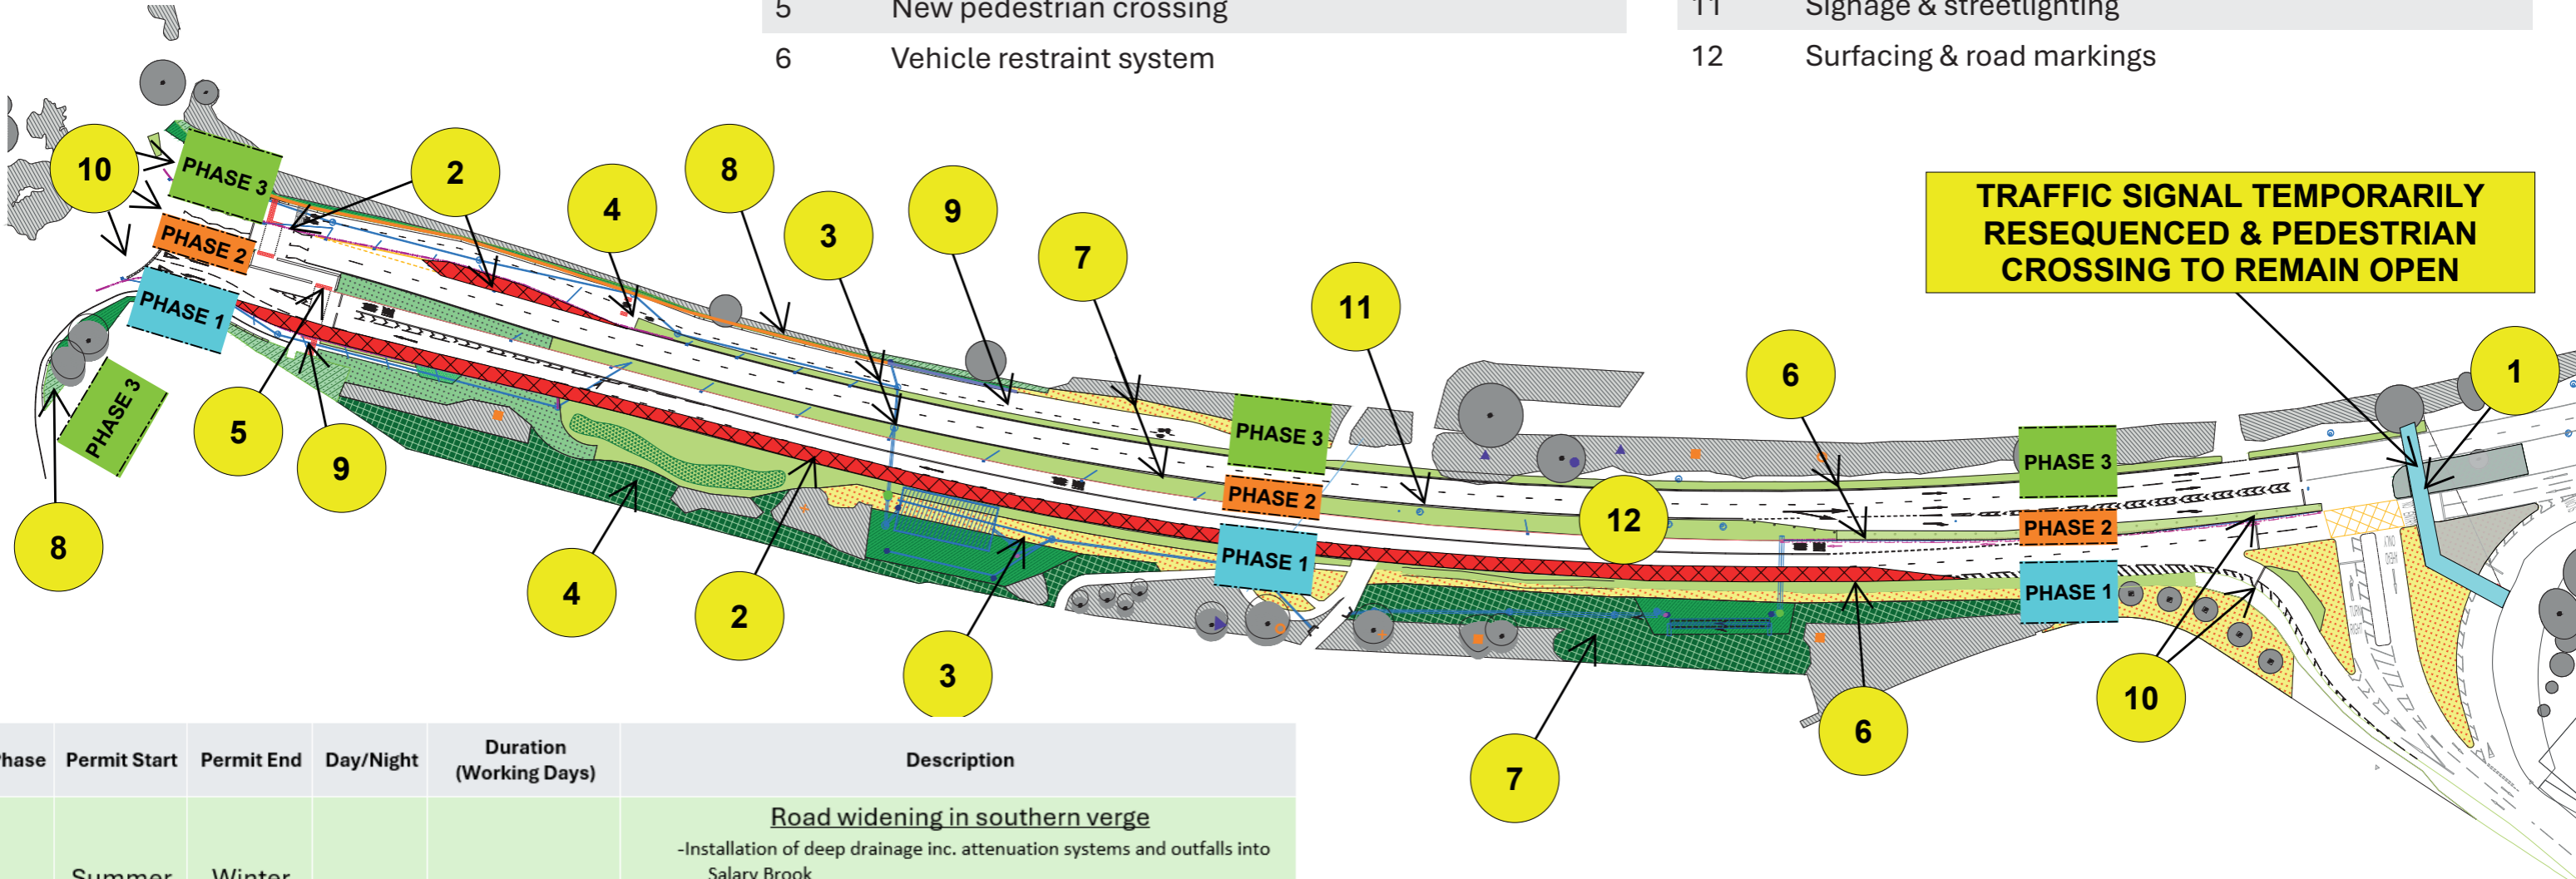

Phase	Permit Start	Permit End	Day/Night	Duration (Working Days)	Description
1	Summer 24	Winter 24	Day	70.00	<u>Road widening in southern verge</u> -Installation of deep drainage inc. attenuation systems and outfalls into Salary Brook -Earthworks to reshape embankments -Excavation of Road Box and construction of widened carriageway inc. surfacing -Landscaping
2	Winter 24	Spring 25	Day	60.00	<u>Central reservation works</u> -Construction of new pedestrian crossing -Installation of surface water drainage -Construction of new kerbline -Installation of VRS -Landscaping
3	Spring 25	Summer 25	Day	90.00	<u>Northern verge works</u> -Construction of piled retaining wall (King Post) inc. Earthworks -Construction of new footway and cycleway -Installation of surface water drainage -Construction of widened Bus Stop -Landscaping
4	Summer 25	Summer 25	Night	10.00	<u>Planing &amp; Surfacing Works</u> -Planing & Surfacing works
