

MORGAN SINDALL

Edinburgh Way – Drainage Works Kwik Fit to Harlow Mill Roundabout

Drainage works have progress along the North side of Edinburgh Way opposite the Gates Ford garage. Those of you who pass the scheme regularly will have seen that we are now installing our large 1500mm diameter drainage pipes along with the 2700mm diameter catch pits. This system works as an attenuation system meaning it will store water before releasing it into the local water course at a set flow rate.










MORGAN SINDALL

Edinburgh Way – HSS – Marshall Skoda

Following the completion of the BT Openreach Works drainage installation has commenced along the North side of Edinburgh Way between HSS & Marshall Skoda. We have completed 50% of the 750mm diameter drainage

pipe.

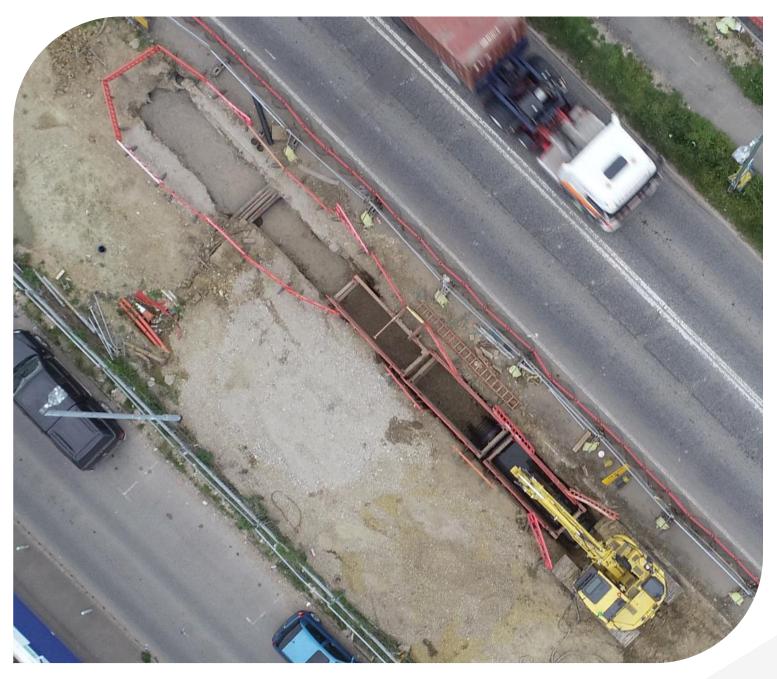






A414 Edinburgh Way

MORGAN SINDALL

Harlow Mill Roundabout Working Area Layout Sketch

Q1 – Q5 are the working areas we refer to for our site works around Harlow Mill Roundabout. These areas are referenced in the following slides.

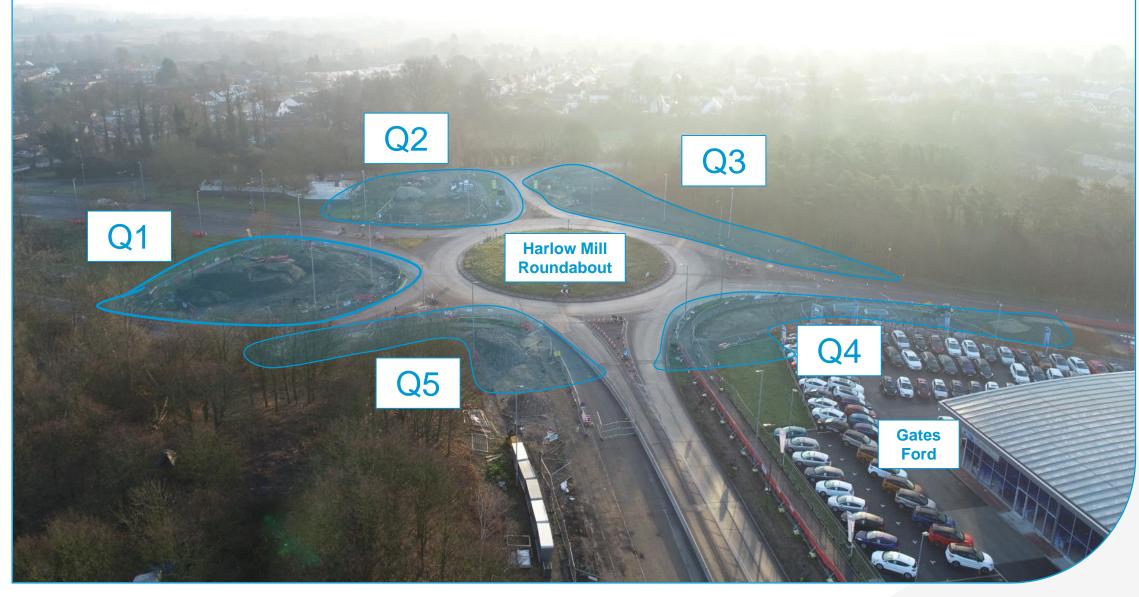






MORGAN SINDALL

A414 Edinburgh Way Latest progress – April 2019

Edinburgh Way – Road Box Construction

We have completed the construction of the road box to Q1 of Harlow Mill roundabout. This includes the installation of kerbs, drainage kerbs and footpath kerbs. Adjusting existing manholes and completing the final trim to the sub base in preparation for temporary surfacing during May.

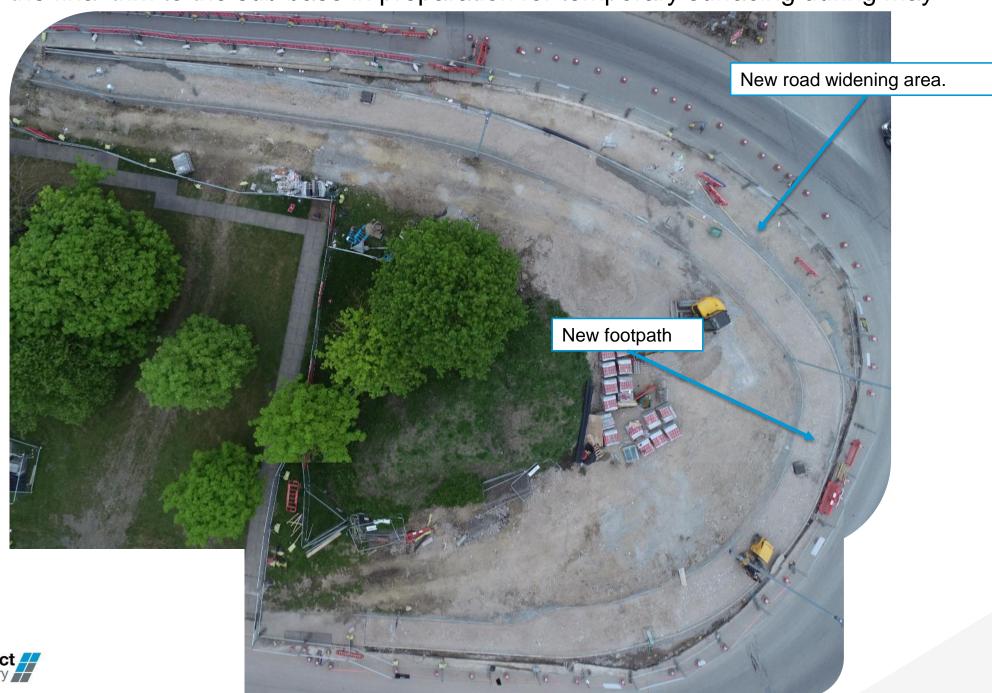



A414 Edinburgh Way Where to find out more



Further details about the scheme can be found on the Essex County Council website at:

- https://www.essexhighways.org/highway-schemes-and-developments/major-schemes/a414-edinburgh-way-cambridge-road.aspx
- Alternatively click on the QR code provided.
- Information about other works in the area can be found at: www.roadworks.org or via the QR code on the right.

For general enquiries, please contact the Essex County Council customer service team:

- By telephone 0345 603 7631
- Online: http://essex.gov.uk/enquiries
- Or use the QR code provided






A414 Edinburgh Way Looking into the future



We have now created a full visualisation of how the finished scheme will look. Please scan the QR code below or use the link to look into the future.

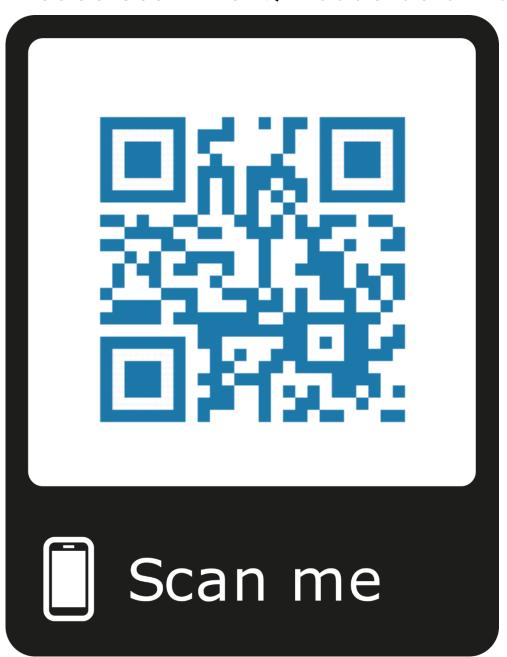

https://youtu.be/8dUmeeqYn1g





A414 Edinburgh Way Edinburgh Way – North side

Planned activities May 2019



Phase

North side phase 1

North side phase 2

North side phase 3

Main Works

- Commence installation of the drainage works.
- Continue installation of the drainage works.
- Continue with drainage installation.
- Road box excavation to the north side of Harlow Mill Roundabout.





A414 Edinburgh Way

Edinburgh Way – South side

Planned activities May 2019




Phase	Utility Diversions	Main Works
South side phase 1	Openreach cable pulling and connectionsVodafone cable installation	None
South side phase 2	Openreach cable box installationVodafone cable installation	None
South side phase 3	Openreach cable box installationVodafone cable installation	None
South side phase 4	 Vodafone Ducts 	 Complete back fill to the crib wall outside Gates Ford and commence drainage installation.





A414 Edinburgh Way Phase Sections



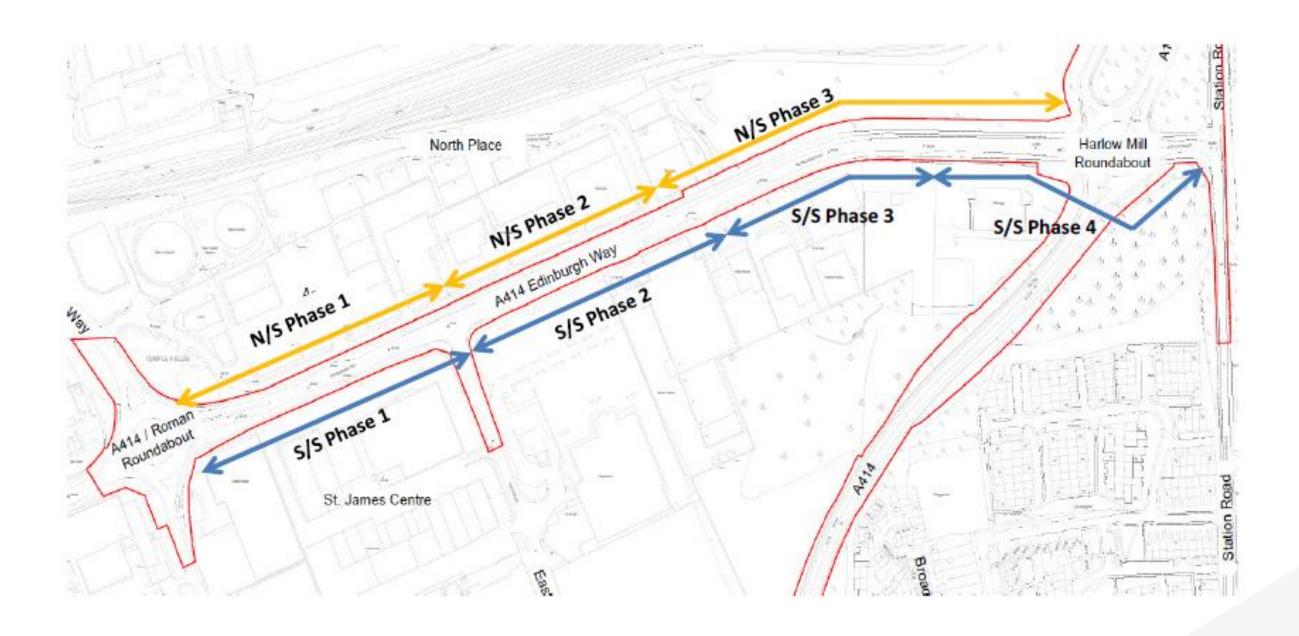





A414 Edinburgh Way

No Right Turn Signs





There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.



