

## A414 Edinburgh Way

Latest progress – March 2019

### Edinburgh Way – Drainage Works

Drainage works have progress along the North side of Edinburgh Way opposite the Gates Ford garage. During March we found some unexpected existing pipes in the ground that held us up for a short while before continuing. We have installed a further two catch pits along with 70 metres of 450mm diameter plastic drainage pipe.



## A414 Edinburgh Way

### Harlow Mill Roundabout Working Area Layout Sketch

Q1 – Q5 are the working areas we refer to for our site works around Harlow Mill Roundabout. These areas are referenced in the following slides.



## A414 Edinburgh Way

Latest progress – March 2019

### Edinburgh Way – Road Box Construction

We have commenced the excavation and construction of the road widening to Harlow Mill roundabout. We have started in Q1 where we have excavated to formation and constructed the foundation for the new road to be laid on. This has meant that some additional traffic management has had to be installed but hopefully it hasn't impacted your journeys to much.



# A414 Edinburgh Way

## Edinburgh Way – North side

### Planned activities April 2019

#### Phase

#### Utility Diversions

#### Main Works

**North side phase 1**

- None

- Commence installation of the drainage works.

**North side phase 2**

- None

- Commence installation of the drainage works.

**North side phase 3**

- None

- Continue with drainage installation.
- Road box excavation to the north side of Harlow Mill Roundabout.


# A414 Edinburgh Way

Edinburgh Way – South side

Planned activities April 2019

<b>Phase</b>	<b>Utility Diversions</b>	<b>Main Works</b>
<b>South side phase 1</b>	<ul style="list-style-type: none"><li>■ Openreach cable pulling and connections</li><li>■ Vodafone cable installation</li></ul>	<ul style="list-style-type: none"><li>■ None</li></ul>
<b>South side phase 2</b>	<ul style="list-style-type: none"><li>■ Openreach cable box installation</li><li>■ Vodafone cable installation</li></ul>	<ul style="list-style-type: none"><li>■ None</li></ul>
<b>South side phase 3</b>	<ul style="list-style-type: none"><li>■ Openreach cable box installation</li><li>■ Vodafone cable installation</li></ul>	<ul style="list-style-type: none"><li>■ None</li></ul>
<b>South side phase 4</b>	<ul style="list-style-type: none"><li>■ Vodafone Ducts</li></ul>	<ul style="list-style-type: none"><li>■ Complete back fill to the crib wall outside Gates Ford.</li></ul>

# A414 Edinburgh Way Phase Sections

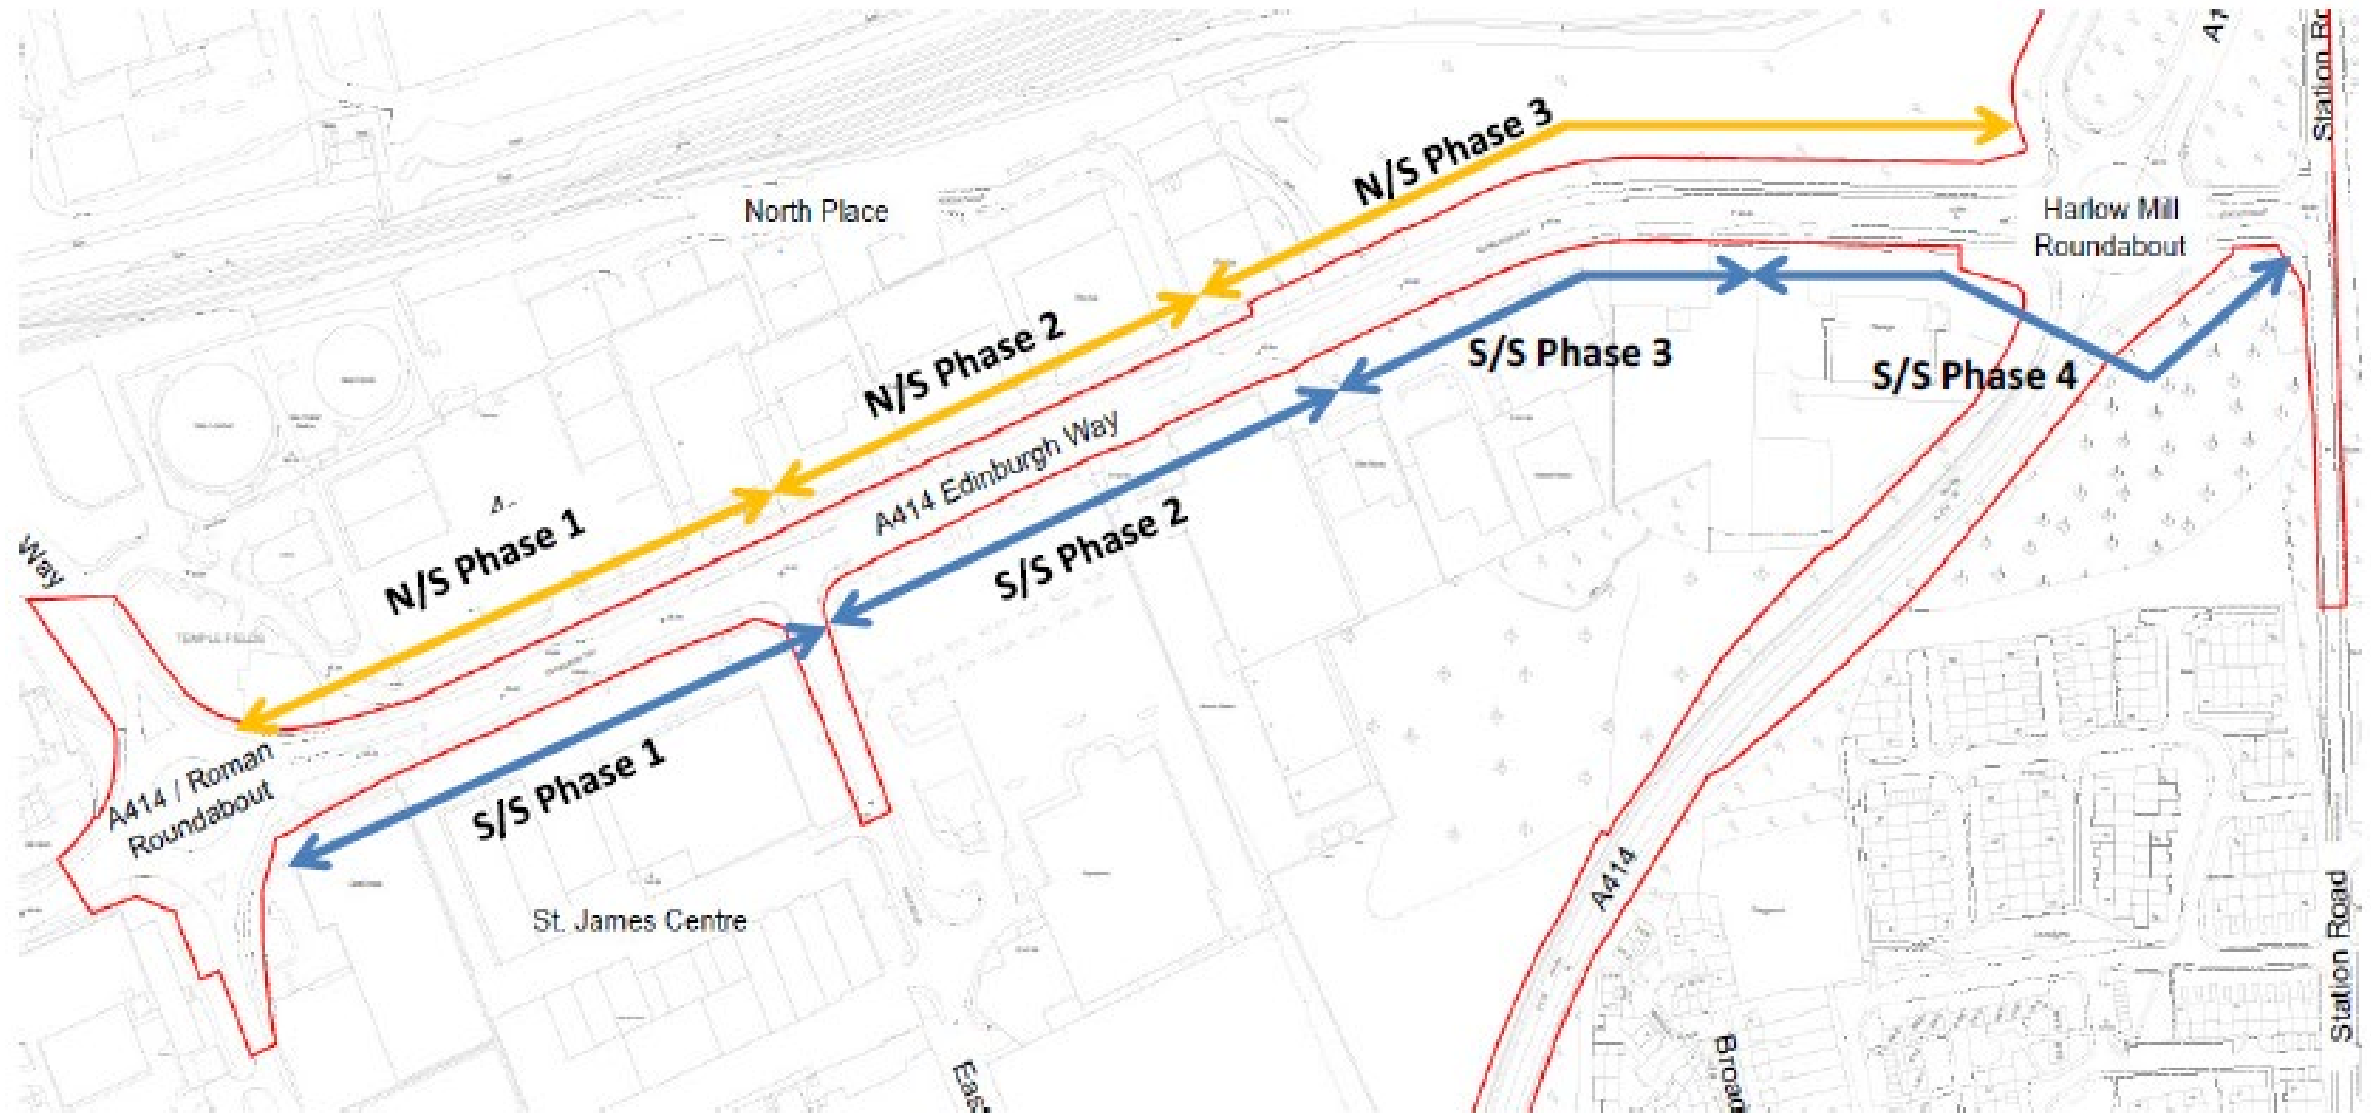

## A414 Edinburgh Way

### No Right Turn Signs



There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.

# A414 Edinburgh Way

## Looking into the future

We have now created a full visualisation of how the finished scheme will look. Please scan the QR code below or use the link to look into the future.



<https://youtu.be/8dUmeeqYn1g>
